
Prowell Woodworks 800.466.1850

PO#25-- -GLASSMAN Dbl Gates Style #72 (2-1/4" thickness)

Viewed on approach from street

Dated Jan 10 2025

DBL GATES #1-- ENTRY COURTYARD

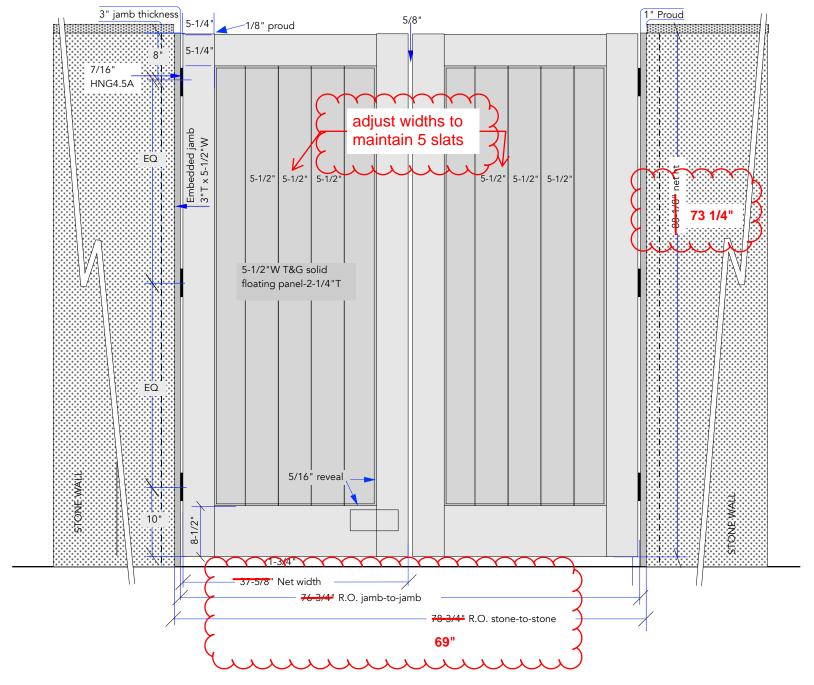

POSTS AND CAPS NOT INCLUDED

GATE #1ENTRY COURTYARD-- - PRODUCT SPECIFICATIONS / NOTES

Product: Garden Gate Style #72 w/2-1/4"T . T&G panel

Material: Clear Western Cedar Construction: Mortise and Tenon

Dimension: R.O: 78-3/8" X 88-1/8" net height

Thickness: 2-1/4"

Swing Direction: IN-SWING

Latch: Site provided Hinge: Site provided

Lead Time: Approx 8 + wks from approval

Ship To: Englewood, CO


Notes:

no t-astrical - why? RH Active per plan.

Viewed on approach from street

Dated Jan 10 2025

DBL GATES #3-- KITCHEN GARDEN

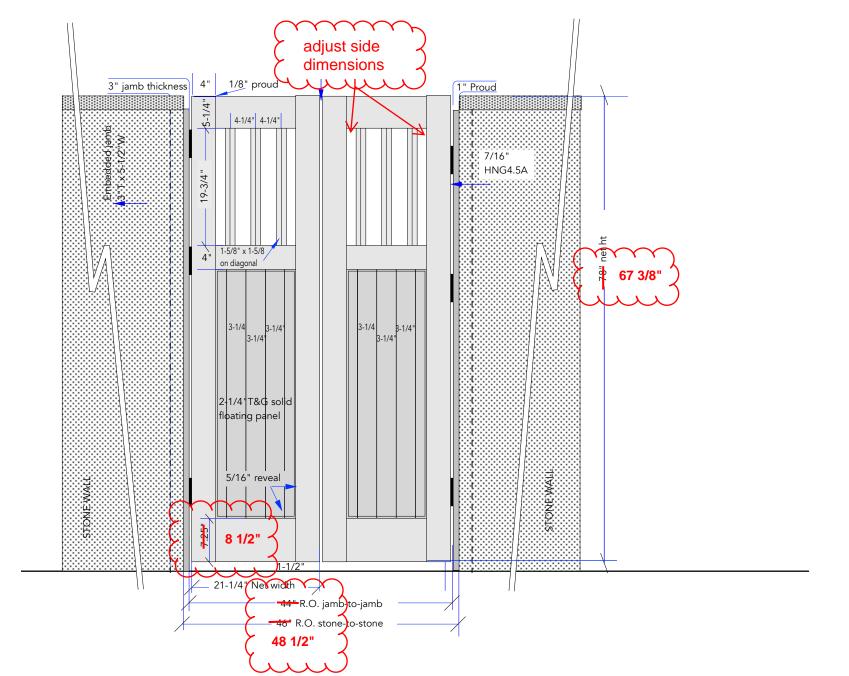

POSTS AND CAPS NOT INCLUDED

Dbl Gate #3 Kitchen Garden-- - Product Specifications / Notes

Product: Garden Gate Style #72 . T&G panel 2-1/4"T

Material: Clear Western Cedar Construction: Mortise and Tenon

Dimension: R.O: 46" X 78" net height

Thickness: 2-1/4"

Swing Direction: IN-SWING

Latch: Site provided Hinge: Site provided


Lead Time: Approx 8 + wks from approval

Ship To: Englewood, CO

Notes:

Dated Jan 10 2025

Viewed on approach from street DBL GATES #6-- AT POOL

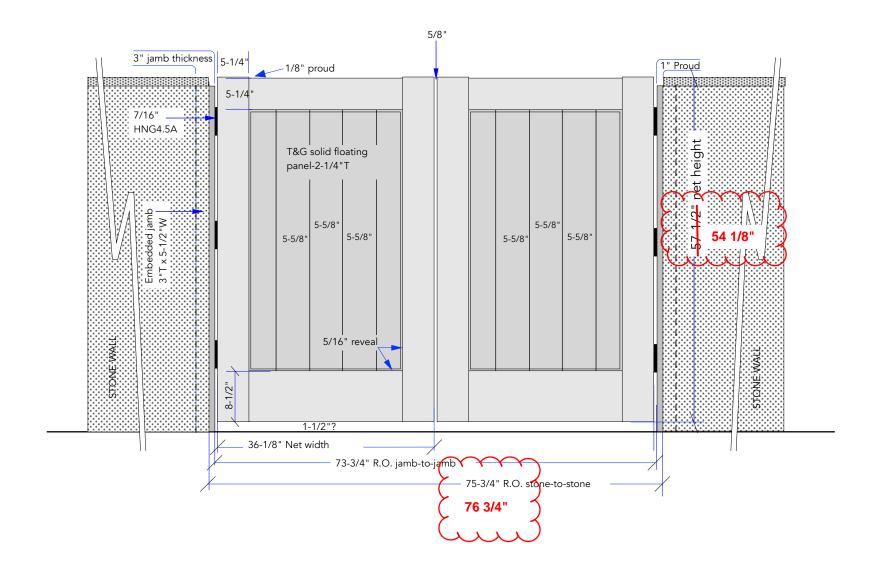

POSTS AND CAPS NOT INCLUDED

Dbl GATE #6 AT POOL -- - PRODUCT SPECIFICATIONS / NOTES

Product: Garden Gate Style #72 . T&G panel 2-1/4"T

Material: Clear Western Cedar Construction: Mortise and Tenon

Dimension: R.O: 75-3/4" X 57-1/2" net height

Thickness: 2-1/4"

Swing Direction: IN-SWING

Latch: Site provided Hinge: Site provided

Lead Time: Approx 8 + wks from approval

Ship To: Englewood, CO

Notes:

no t- astrical?
Plan shows RH active, inswing.


Viewed on approach from street

Dated Jan 10 2025

DBL GATES CARETAKER VESTIBULE

NOTES:

- 1) Mounts to stone or wood posts?
- 2) verify R.O. width and net ht

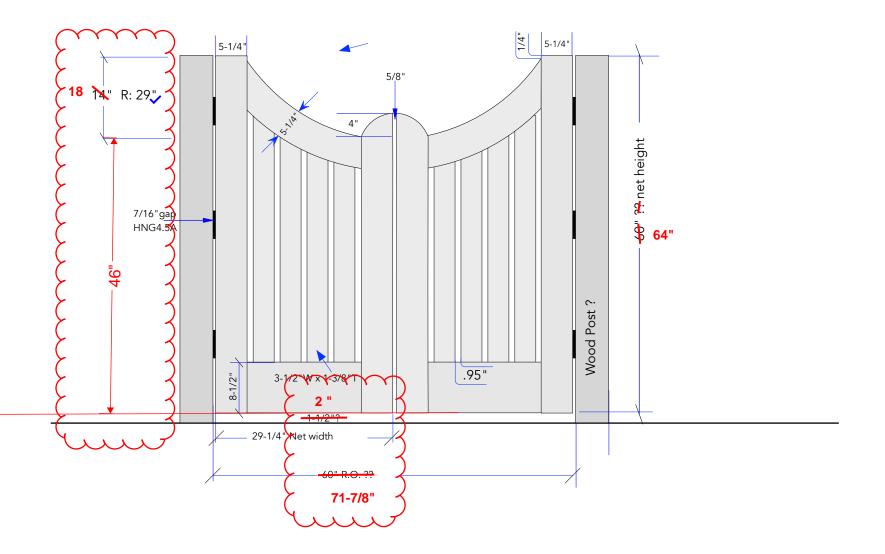

POSTS AND CAPS NOT INCLUDED

Dbl Gates Caretaker's Vestibule -- - Product Specifications / Notes

Product: Garden Gate Style #72 . T&G panel 2-1/4"T

Material: Clear Western Cedar Construction: Mortise and Tenon

Dimension: R.O: 60" +/- X 60" +/- net height to springline

Thickness: 1-5/8" 2-1/4"
Swing Direction: IN-SWING

Latch: Site provided Hinge: Site provided

Lead Time: Approx 8 + wks from approval

Ship To: Englewood, CO

Notes:
